MavWalk – Iteration 2 Update

Iteration 1 Recap

01 Delivered initial UI mockups (login, request, tracking, active walk)

02 Defined risks, MoSCoW priorities, and roadmap

03 Feedback: add risks, show clearer user flow, improve documentation, more routes

04 Pivot: from police-integration → simpler student-centered website

Why the Pivot?

- Police escort integration was too complex and needed external dependencies
- Parking & Transportation feedback: low feasibility
- Pivot allows progress, so we decided with a leaner design, faster prototype, student-focused

Iteration 2 Goals

Build MVP foundation:

- **Pivot to a student well-being and navigation app**
- **Design a user flow centered on positive messaging**
- **Create high-fidelity UI mockups for the new app experience**
- **Refine project scope and roadmap**

Live Demo time!

Final UI mockup

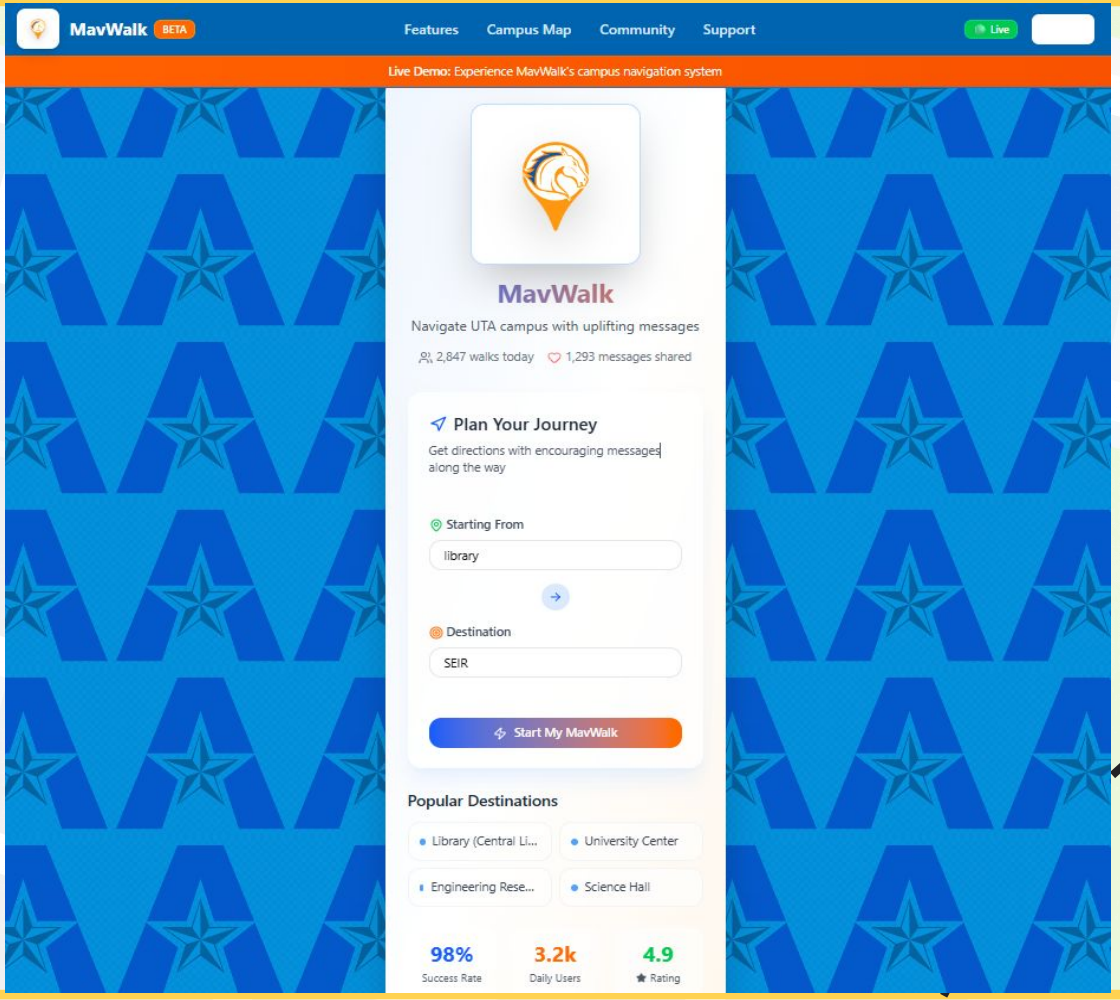

When user starts the walk

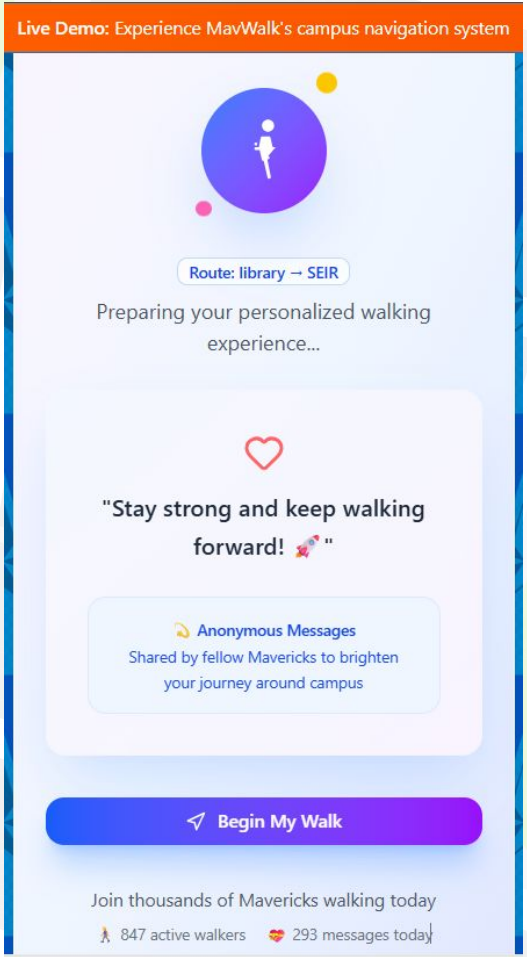

Live walk progress page

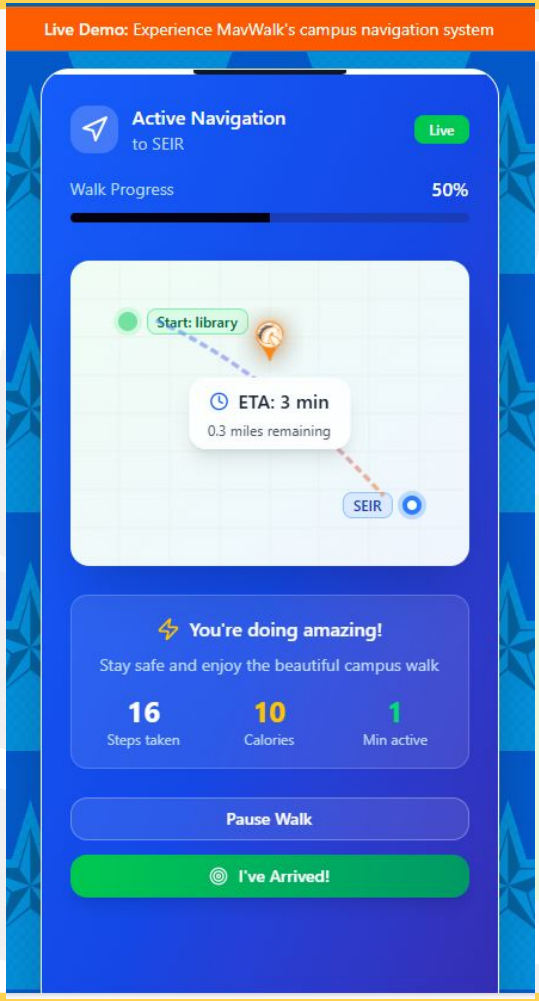

End of the walk

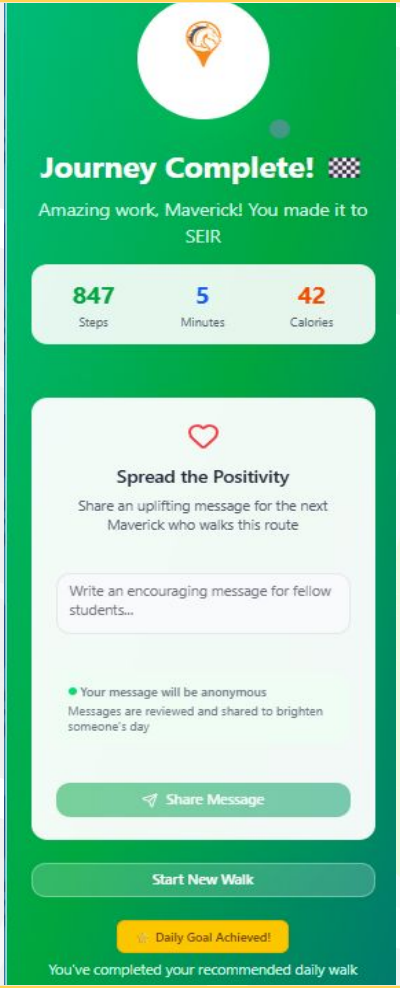

Risks & Mitigation

Risk	Risk Description	Category	P(0-1)	E(Impact)	RE	Why it matters	Mitigation	Contingency
R1	Wrong functionality / misaligned with student needs	Business	0.5	100	50.0	Main risk identified in slides, building features without user feedback	Early student feedback via beta test and QR survey	If feedback negative, refine routes and message concepts
R2	Low adoption / engagement	Business	0.7	40	28.0	App depends on students actually using it	Simplify UI; no login; promote via dorms and library posters	Refocus on single popular route first or engage in lots of on campus advertisement
R3	Technical bug / map integration failure	Technical	0.6	20	12.0	Third-party API or map rendering failure	Use static JSON routes and offline testing	Fallback to screenshot map display
R4	Accessibility / usability failures	Quality	0.3	40	12.0	Affects inclusivity and grading	Mobile-first design; test WCAG AA	Increase font/contrast if needed
R5	Team member availability / burnout	Resource	0.9	8	7.2	Everyone has other classes and jobs	Shared calendar and light PR cycle	Redistribute workload
R6	Performance issues (> 2s load)	Technical	0.5	10	5.0	Slow load time affects user satisfaction	Cache routes; compress assets	Fallback to static map
R7	Inappropriate content (submitted messages)	Content/ Security	0.5	8	4.0	Could violate UTA guidelines or harm reputation	Use only curated messages for MVP	Disable ‘submit message’ feature and update filtering algorithm

Roadmap

Iteration 2 (Now): Prototype with core features, Refactoring

Iteration 3 (Next): Integration & Testing, Connecting Front-end API with Backend database server

Conclusion

- Iteration 2 delivers MVP foundation
- Pivot makes solution simpler & student-centered
- Sets stage for Iteration 3 enhancements and near-final product
- https://github.com/ceh6514/MavWalk
